




STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND
DURING SEWER WORK					
Sloat Ave. to Wawona St.	9AM – 3PM (M-F) Continuous during Sewer Lining Work	2@10' 2@10'	2@10' 2@10'	- -	- -
*(MC), ★, □, ▢	At Other Times	Full Roadway	Full Roadway	-	-
Wawona St. to Vicente St.	7AM – 5PM (M-F) At Other Times	2@10' Full Roadway	2@10' Full Roadway	- -	- -
*(MC)					
CROSS STREETS for 19TH AVENUE					
Sloat Blvd. *(MC), β	7AM – 5PM (M-F) At Other Times	- -	- -	2@11' Full Roadway	3@10' Full Roadway
Wawona St. β.	7AM – 5PM (M-F) At Other Times	- -	- -	1 @ 10' Full Roadway	1@10' Full Roadway
Vicente St β	7AM – 5PM (M-F) At Other Times	- -	- -	1@10' Full Roadway	1@10' Full Roadway

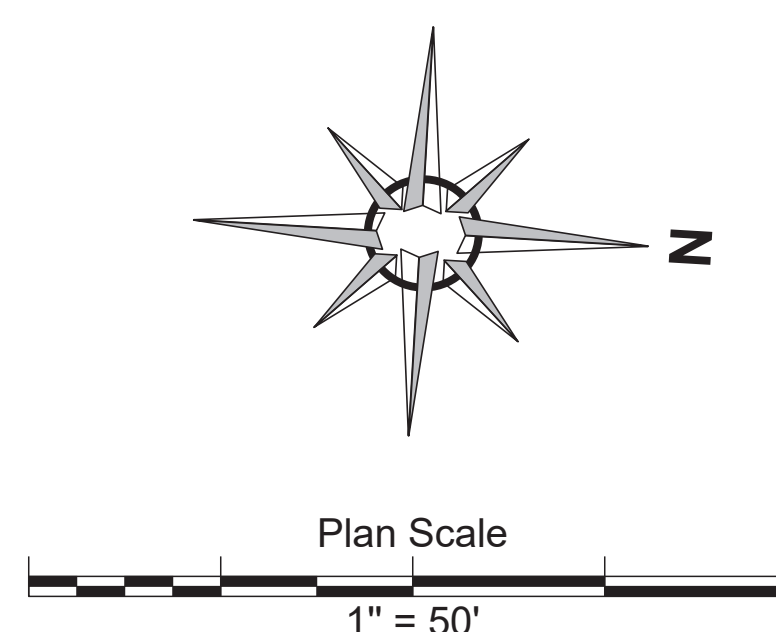

Date: 03/16/2022 **Author:** RC/CM **Project:** 19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT
Client: JMB CONSTRUCTION **Location:** SAN FRANCISCO **TCP:** 205
CMC Job #: 2530

<p>Comments:</p> <p>1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS TABLE</p> <p>2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.</p> <p>3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.</p> <p>4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.</p> <p>5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.</p> <p>6) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.</p> <p>7) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREET ON WHICH THERE IS CONSTRUCTION.</p> <p>8) THE CONTRACTOR SHALL NOT WORK ON CURB RAMPS AT DIAGONALLY LOCATED CORNERS AT THE SAME TIME IF THERE IS SIDEWALK WORK OR UNLESS OTHERWISE INSTRUCTED BY THE TRAFFIC ENGINEER.</p>
--
