


TRAFFIC CONTROL PLAN  
19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT  
AWSS WORK - 19TH AVE AT ULLOA ST

CONTRACTOR TO ACTIVATE CMS BOARD  
2 WEEKS IN ADVANCE TO NOTIFY  
UPCOMING MAJOR TRAFFIC DELAY AND  
USE OF ALTERNATE ROUTES

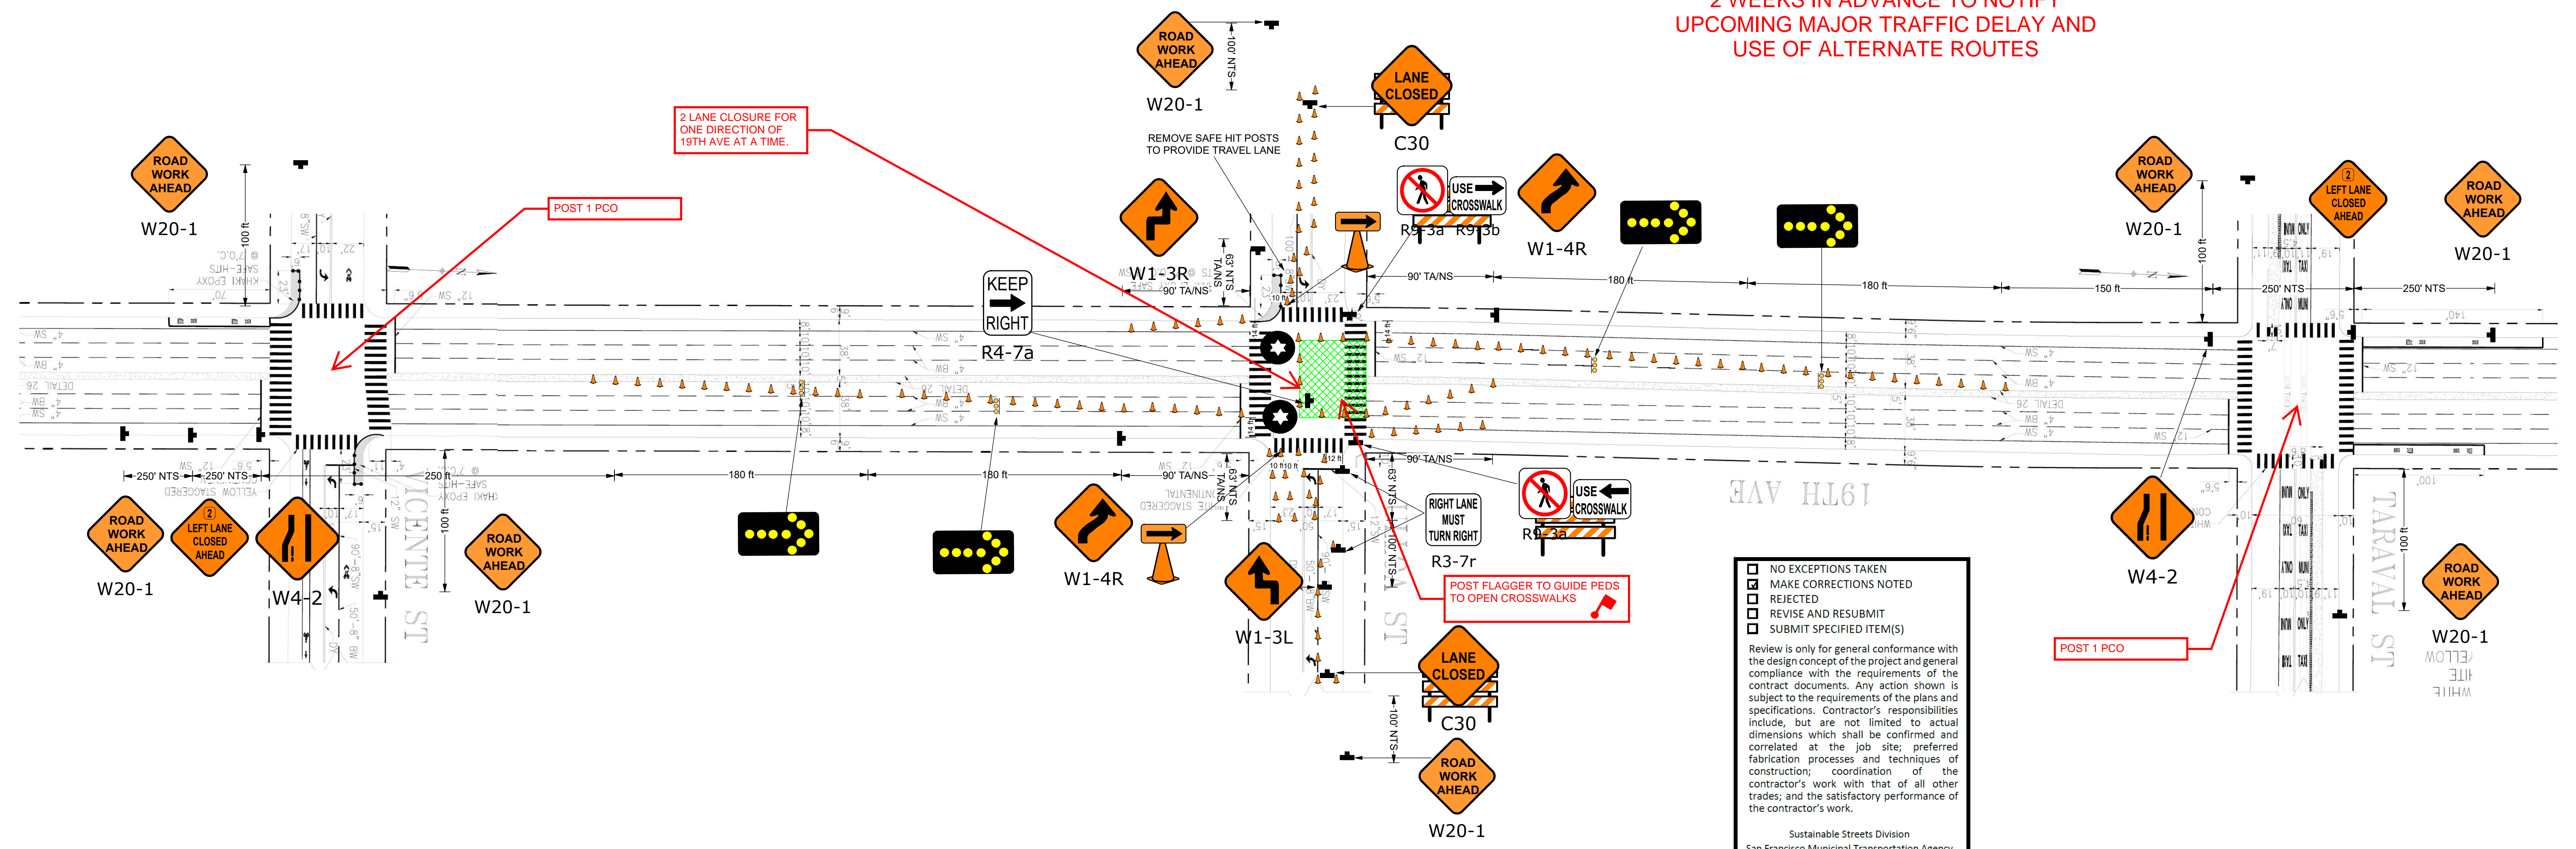

☐ NO EXCEPTIONS TAKEN  
☒ MAKE CORRECTIONS NOTED  
☐ REJECTED  
☐ REVISE AND RESUBMIT  
☐ SUBMIT SPECIFIED ITEM(S)


Review is only for general conformance with the design concept of the project and general compliance with the requirements of the contract documents. Any action shown is subject to the requirements of the plans and specifications. Contractor's responsibilities include, but are not limited to actual dimensions which shall be confirmed and correlated at the job site; preferred fabrication processes and techniques of construction; coordination of the contractor's work with that of all other trades; and the satisfactory performance of the contractor's work.

Sustainable Streets Division  
San Francisco Municipal Transportation Agency  
City and County of San Francisco

By: *[Signature]* Date: 07/20/2021

- Legend**
- Type III Barricade
  - 28" Traffic Cone
  - Delineator
  - Pedestrian Barricade
  - Work Area
  - Sign and Stand
  - Direction of Travel
  - Concrete K-Rail
  - Crash Cushion
  - NTS Not To Scale
  - T/ANS Tow-Away/No Stopping
  - Parking Control Officer
  - Flagger
  - Type I Barricade
  - Flashing Beacon

STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND
DURING AWSS MONITORING, REMOVAL AND NEW WORK					
19TH AVENUE					
Vicente St. to Ulloa St. *(MC)	7AM - 5PM (M-F) removal and monitoring work	2 @ 10'	Full Roadway	-	-
	9AM - 3PM (M-F) new work	1 @ 14'	3 @ 10'		
	3PM - 5PM (M-F) new work	2 @ 10'	3 @ 10'		
	At Other Times	Full Roadway	Full Roadway		
Ulloa St. to Taraval St. *(MC)	7AM - 5PM (M-F) removal and monitoring work	2 @ 10'	Full Roadway	-	-
	9AM - 3PM (M-F) new work	3 @ 10'	1 @ 14'		
	3PM - 5PM (M-F) new work	3 @ 10'	2 @ 10'		
	At Other Times	Full Roadway	Full Roadway	-	-
CROSS STREETS for 19TH AVENUE					
Ulloa St. *	7AM - 5PM (M-F) monitoring work	-	-	1 @ 10'	1 @ 10'
	7AM - 5PM (M-F) removal and new work			Closed @ (west leg) 1 @ 10' (east leg)	1 @ 10' (east leg)
	At Other Times	-	-	Full Roadway	Full Roadway



3450 3RD ST #3G  
SAN FRANCISCO, CA 94124  
415-206-1700 PHONE  
415-206-1711 FAX  
INFO@CMCTRAFFIC.COM

LICENSE NO 792059  
CLASS A, 31, C21  
WBE/SBE/LBE/DBE CERTIFIED  
WWW.CMCTRAFFIC.COM

Date: 05/07/2021 Author: RC/CM Project: 19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT  
Client: JMB CONSTRUCTION Location: SAN FRANCISCO TCP: 076  
CMC Job #: 2530 REV: 1

**Comments:**

- 1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS TABLE
- 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
- 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.
- 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
- 5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
- 6) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.
- 7) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREET ON WHICH THERE IS CONSTRUCTION.
