


STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND
		DURING SEWER WORK			
Noriega St. to Moraga St. '(MC) ★	7AM – 5PM (M-F)	2@10'	2@10'	-	-
	9AM – 3PM (M-F)	1@14'	1@14'	-	-
	Sewer Crossing 19 th Ave. @ Noriega St. At Other Times	Full Roadway	Full Roadway	-	-
Moraga St. to Lawton St. '(MC)	7AM – 5PM (M-F)	Full Roadway	2@10'	-	-
	At Other Times		Full Roadway	-	-
Lawton St. to Kirkham St. '(MC), ★, ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-
	9AM – 3PM (M-F)	1@14'	1@14'	-	-
	Sewer Crossing 19 th Ave. @ Kirkham At Other Times	Full Roadway	Full Roadway	-	-
Kirkham St. to Judah St. '(MC) ★	7AM – 5PM (M-F)	3@10'	2@10'	-	-
	9AM – 3PM (M-F)	1@14'	1@14'	-	-
	Sewer Crossing 19 th Ave. @ Kirkham St. & Kirkham – 3PM (M-F) Sewer Crossing 19 th Ave. @ Judah St. & At Other Times	1@14'	2@10'	-	-
Judah St. to Irving St. '(MC), ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-
	9AM – 3PM (M-F)	1@14'	2@10'	-	-
	Sewer Crossing 19 th Ave. @ Judah St. & At Other Times	Full Roadway	Full Roadway	-	-
Irving St. to Lincoln Way '(MC), ★, ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-
	At Other Times	Full Roadway	Full Roadway	-	-
CROSS STREETS for 19th AVENUE					
Noriega St. ★	7AM – 3PM (M-F)	-	-	Closed ☉	Closed ☉
	At Other Times	-	-	Full Roadway	Full Roadway
Moraga St β	7AM – 5PM (M-F)	-	-	1@12'	Closed ☉
	At Other Times	-	-	Full Roadway	Full Roadway
Lawton St β	7AM – 5PM (M-F)	-	-	1@12'	Closed ☉
	At Other Times	-	-	Full Roadway	Full Roadway
Kirkham St β ★, ★★, ◆	7AM – 3PM (M-F)	-	-	1@12'	◆, ◆
	At Other Times	-	-	Full Roadway	Full Roadway
Judah St. '(MM)	7AM – 3PM (M-F)	-	-	Closed ☉ (Except Muni)	Closed ☉ (Except Muni)
	At Other Times	-	-	Full Roadway	Full Roadway
Irving St. ★	7AM – 3PM (M-F)	-	-	1@10'	1@10'
	At Other Times	-	-	Full Roadway	Full Roadway
Lincoln Way '(MC), ★, ☐	9AM – 3PM (M-F)	-	-	1@14'	2@11'
	During Sewer Lining	-	-	2@10'	2@10'
	At Other Times	-	-	Full Roadway	Full Roadway

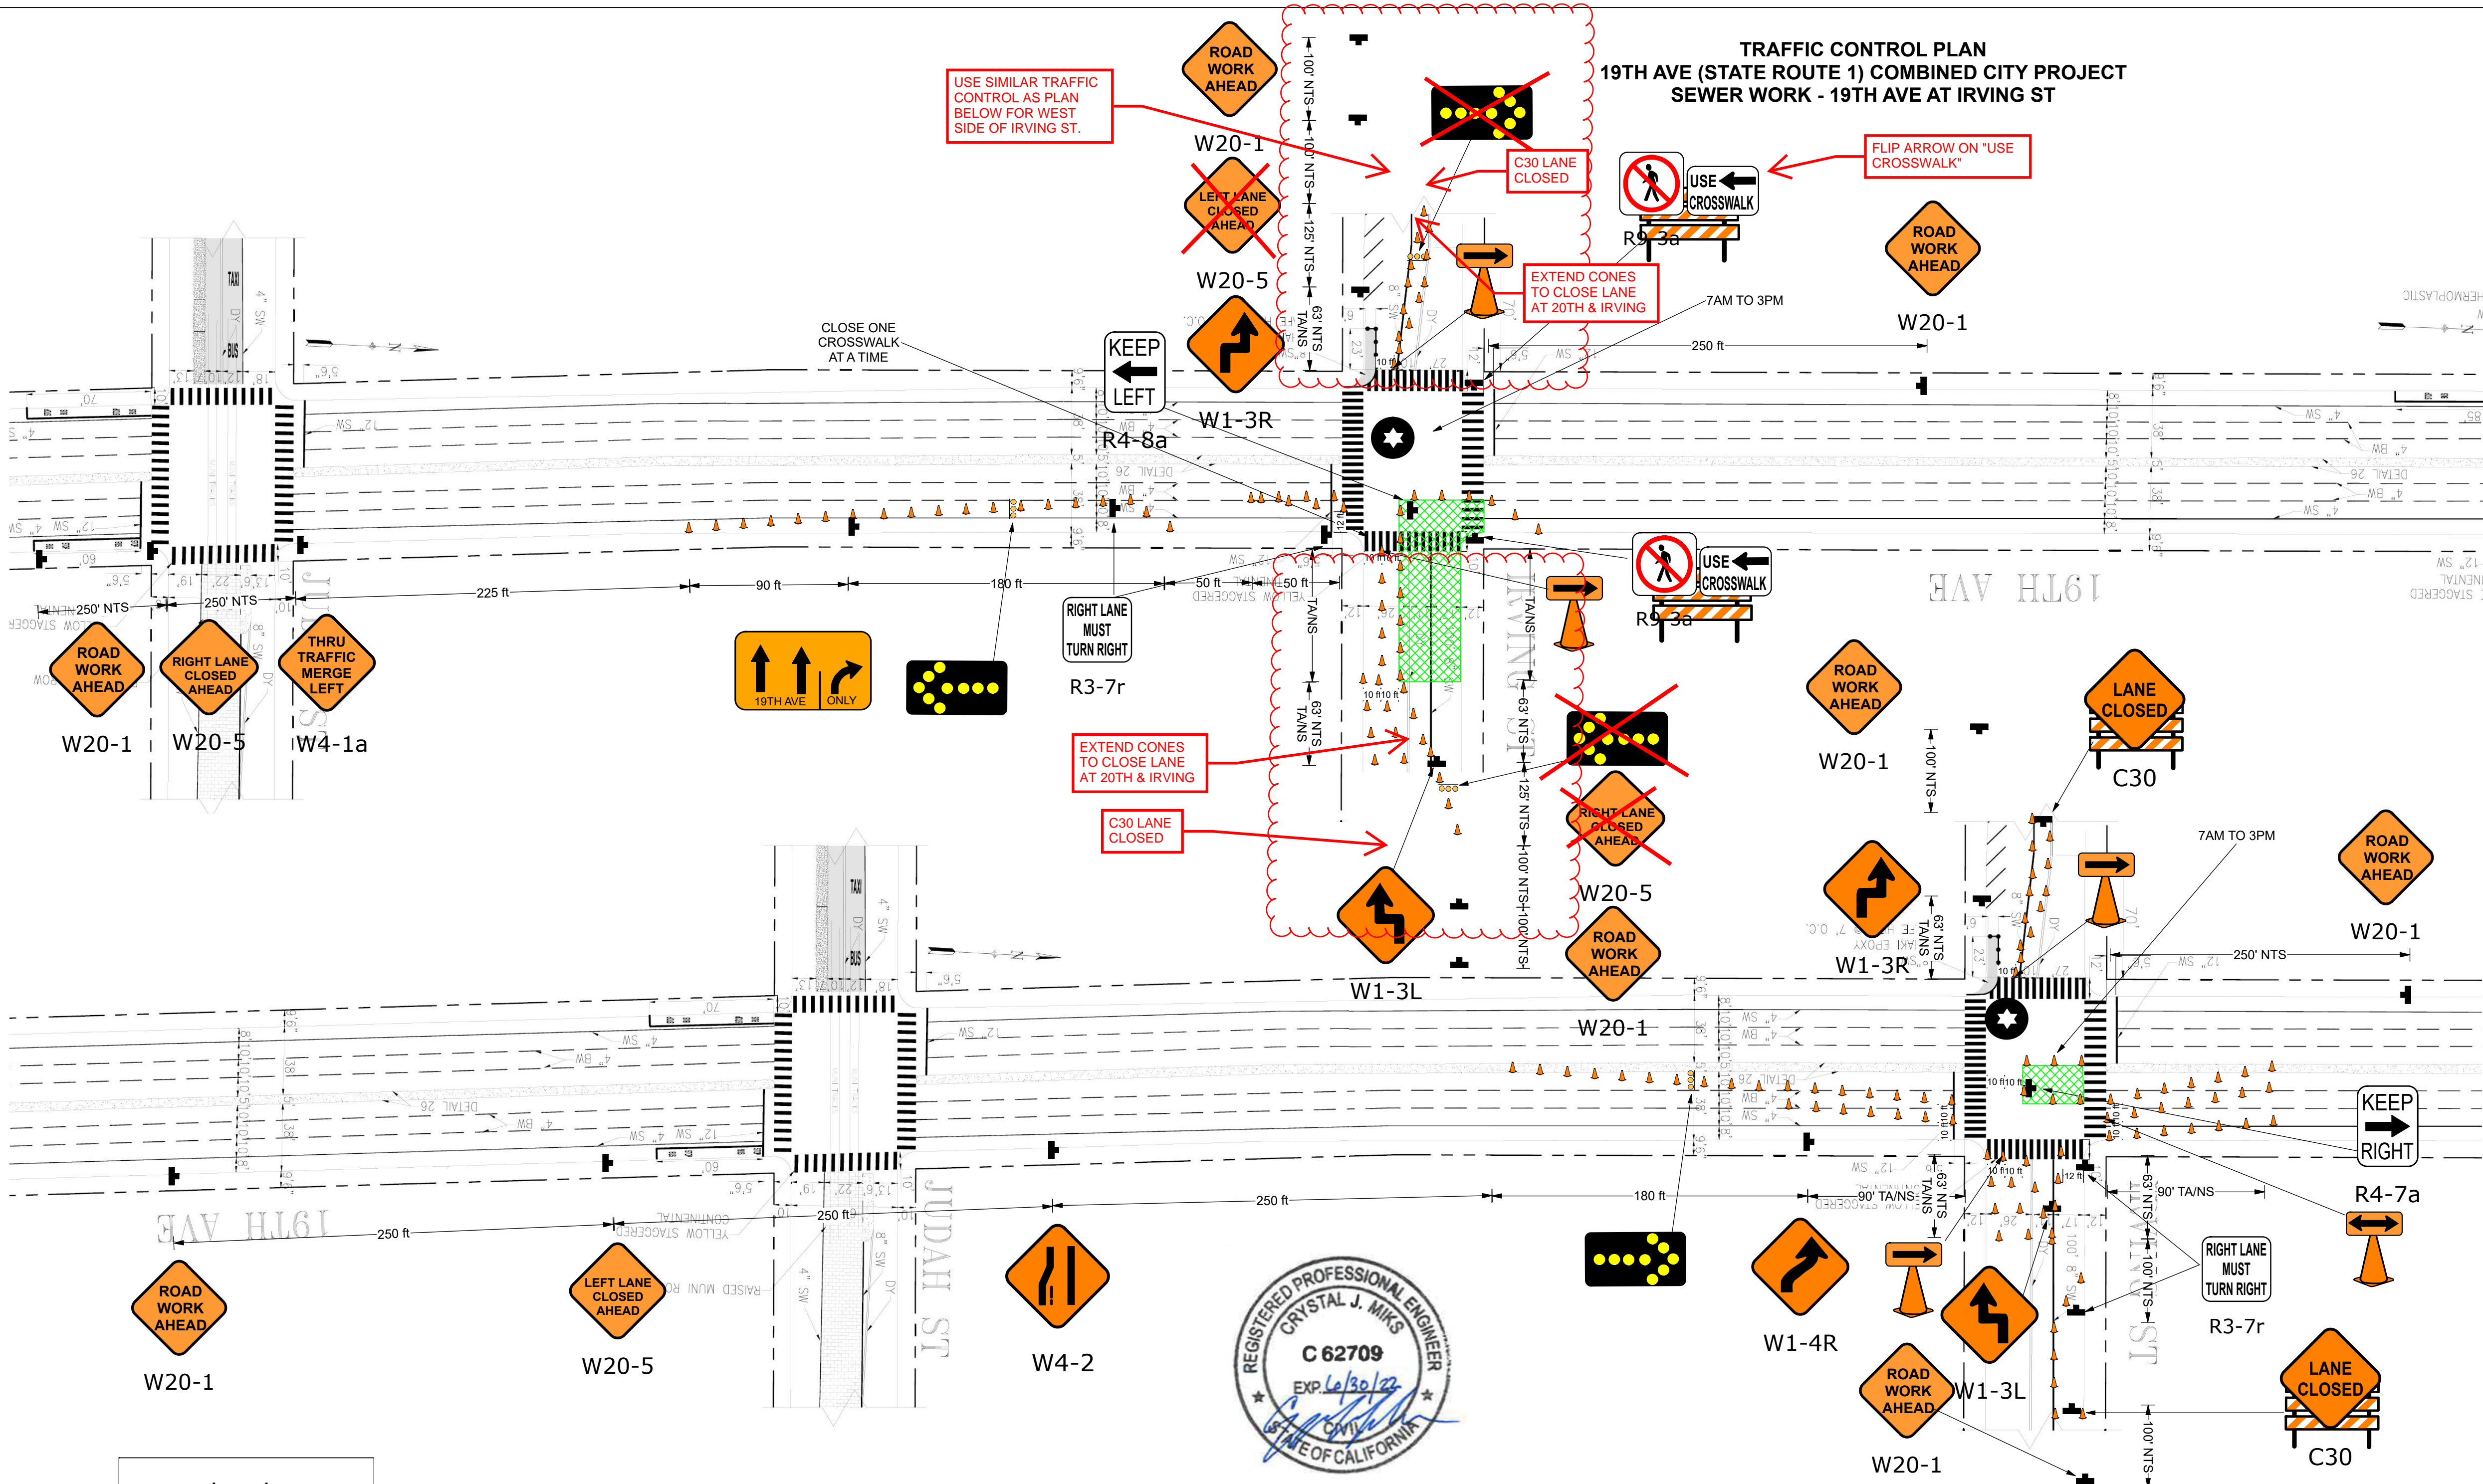

STREET	TIME	NORTHBOUND	SOUTHBOUND	EASTBOUND	WESTBOUND	
		DURING SEWER WORK				
Noriega St. to Moraga St. (MC) ★	7AM – 5PM (M-F)	2@10'	2@10'	-	-	
	9AM – 3PM (M-F)	1@14'	1@14'	-	-	
	Sewer Crossing 19 th Ave. @ Noriega St.					
	At Other Times	Full Roadway	Full Roadway	-	-	
Moraga St. to Lawton St. (MC)	7AM – 5PM (M-F)	Full Roadway	2@10'	-	-	
	At Other Times		Full Roadway	-	-	
Lawton St. to Kirkham St. (MC), ★, ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-	
	9AM – 3PM (M-F)	1@14'	1@14'	-	-	
	Sewer Crossing 19 th Ave. @ Kirkham					
	At Other Times	Full Roadway	Full Roadway	-	-	
Kirkham St. to Judah St. (MC) ★	7AM – 5PM (M-F)	3@10'	2@10'	-	-	
	9AM – 3PM (M-F)	1@14'	1@14'	-	-	
	Sewer Crossing 19 th Ave. @ Kirkham St. & Kirkham	1@14'	2@10'	-	-	
	At Other Times	Full Roadway	Full Roadway	-	-	
Judah St. to Irving St. (MC), ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-	
	9AM – 3PM (M-F)	1@14'	2@10'	-	-	
	Sewer Crossing 19 th Ave. @ Judah St. &					
	At Other Times	Full Roadway	Full Roadway	-	-	
Irving St. to Lincoln Way (MC), ★, ☐	7AM – 5PM (M-F)	2@10'	2@10'	-	-	
	At Other Times	Full Roadway	Full Roadway	-	-	
CROSS STREETS FOR 19 th AVENUE						
Noriega St. ★	7AM – 3PM (M-F)	-	-	Closed ☉	Closed ☉	
	At Other Times	-	-	Full Roadway	Full Roadway	
Moraga St β	7AM – 5PM (M-F)	-	-	1@12'	Closed ☉	
	At Other Times	-	-	Full Roadway	Full Roadway	
Lawton St β	7AM – 5PM (M-F)	-	-	1@12'	Closed ☉	
	At Other Times	-	-	Full Roadway	Full Roadway	
Kirkham St β ★, ★★, ★	7AM – 3PM (M-F)	-	-	1@12' ★, ★		
	At Other Times	-	-	Full Roadway	Full Roadway	
Judah St. (MM)	7AM – 3PM (M-F)	-	-	Closed ☉ (Except Muni)	Closed ☉ (Except Muni)	
	At Other Times	-	-	Full Roadway	Full Roadway	
Irving St. ★	7AM – 3PM (M-F)	-	-	1@10'	1@10'	
	At Other Times	-	-	Full Roadway	Full Roadway	
Lincoln Way (MC), ★, ☐	9AM – 3PM (M-F)	-	-	1@14'	2@11'	
	During Sewer Lining	-	-	2@10'	2@10'	
	At Other Times	-	-	Full Roadway	Full Roadway	

Date: 10/29/2020 **Author:** RC/CM **Project:** 19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT
Client: JMB CONSTRUCTION **Location:** SAN FRANCISCO **TCP:** 003
CMC Job #: 2530 **REV:** 1

Comments:

- 1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS TABLE.
- 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
- 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.
- 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
- 5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
- 6) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.
- 7) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREET ON WHICH THERE IS CONSTRUCTION.
- 8) PROVIDE FULL ROADWAY AND PLATE ALL OPEN TRENCHES DURING NON-WORKING HOURS. PLACE W8-24 "STEEL PLATE AHEAD" SIGNS IN ADVANCE OF TRENCH PLATES.
- 9) DO NOT OPEN ROADWAY WITH STEPS / RIDGES IN THE PAVEMENT SURFACE >3".
IF STEP / RIDGE IN THE ROADWAY IS PARALLEL TO THE DIRECTION OF TRAVEL AT LANE LINES AND IS >3/8" AND <3" USE W8-11 UNEVEN LANES SIGN.
IF STEP / RIDGE IN THE ROADWAY IS PERPENDICULAR TO THE DIRECTION OF TRAVEL OR PARALLEL, BUT NOT ON LANE LINES AND IS >3/4" AND <3" USE C46 (CA) UNEVEN PAVEMENT SIGN.
- 10) THE OPEN TRENCH (C27(CA)) SIGN SHALL BE USED IN ADVANCE OF OPEN TRENCHES IN/OR ADJACENT TO ROADWAY.

- ☐ NO EXCEPTIONS TAKEN
☒ MAKE CORRECTIONS NOTED
☐ REJECTED
☐ REVISE AND RESUBMIT
☐ SUBMIT SPECIFIED ITEM(S)

Review is only for general conformance with the design concept of the project and general compliance with the requirements of the contract documents. Any action shown is subject to the requirements of the plans and specifications. Contractor's responsibilities include, but are not limited to actual dimensions which shall be confirmed and correlated at the job site; preferred fabrication processes and techniques of construction; coordination of the contractor's work with that of all other trades; and the satisfactory performance of the contractor's work.

Sustainable Streets Division
San Francisco Municipal Transportation Agency
City and County of San Francisco

By MDI Date 11/03/2020



ST #3G LICENSE NO 792059
SACRAMENTO, CA 94124 CLASS A, 31, C21

-1700 PHONE
 -1711 FAX
 CTTRAFFIC.COM

Date: 10/29/2020 **Author:** RC/CM **Project:** 19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT
Client: JMB CONSTRUCTION **Location:** SAN FRANCISCO **TCP:** 003
CMC Job #: 2530 **REV:** 1

Comments:

- 1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS TABLE.
- 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
- 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.
- 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
- 5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
- 6) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.
- 7) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREET ON WHICH THERE IS CONSTRUCTION.
- 8) PROVIDE FULL ROADWAY AND PLATE ALL OPEN TRENCHES DURING NON-WORKING HOURS. PLACE W8-24 "STEEL PLATE AHEAD" SIGNS IN ADVANCE OF TRENCH PLATES.
- 9) DO NOT OPEN ROADWAY WITH STEPS / RIDGES IN THE PAVEMENT SURFACE >3".
IF STEP / RIDGE IN THE ROADWAY IS PARALLEL TO THE DIRECTION OF TRAVEL AT LANE LINES AND IS >3/8" AND <3" USE W8-11 UNEVEN LANES SIGN.
IF STEP / RIDGE IN THE ROADWAY IS PERPENDICULAR TO THE DIRECTION OF TRAVEL OR PARALLEL, BUT NOT ON LANE LINES AND IS >3/4" AND <3" USE C46 (CA) UNEVEN PAVEMENT SIGN.
- 10) THE OPEN TRENCH (C27(CA)) SIGN SHALL BE USED IN ADVANCE OF OPEN TRENCHES IN/OR ADJACENT TO ROADWAY.
