


TRAFFIC CONTROL PLAN
19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT
BUS PAD WORK - 19TH AVE AT TARAVAL ST


WORKING HOURS

Relocate temporary bus stop here

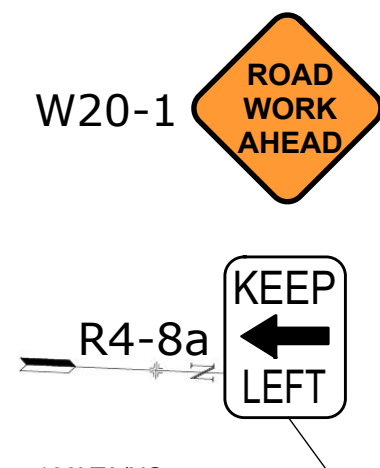

existing bus stop needs to be relocated

RIGHT LANE MUST TURN RIGHT R3-7r



W4-1a

W20-5

W20-1

NO EXCEPTIONS TAKEN
MAKE CORRECTIONS NOTED
REJECTED
REVISE AND RESUBMIT
SUBMIT SPECIFIED ITEM(S)


Review is only for general conformance with the design concept of the project and general compliance with the requirements of the contract documents. Any action shown is subject to the requirements of the plans and specifications. Contractor's responsibilities include, but are not limited to actual dimensions which shall be confirmed and correlated at the job site; preferred fabrication processes and techniques of construction; coordination of the contractor's work with that of all other trades; and the satisfactory performance of the contractor's work.

Sustainable Streets Division
San Francisco Municipal Transportation Agency
City and County of San Francisco

By: *UR* Date: **08/12/2021**

NON-WORKING HOURS

Relocate temporary bus stop here

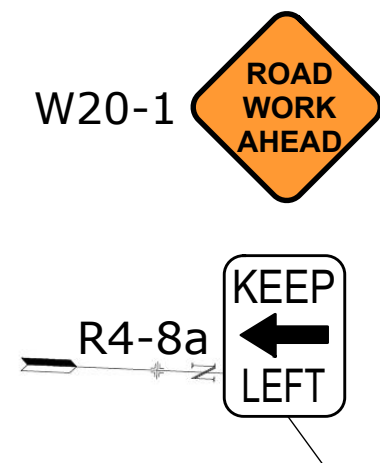

existing bus stop needs to be relocated

RIGHT LANE MUST TURN RIGHT R3-7r



W4-1a

W20-5


W20-1



Traffic Lane Requirements
Number and Width of Lanes for Through Traffic

| STREET | TIME | NORTHBOUND | SOUTHBOUND | EASTBOUND | WESTBOUND |
|---------------------------------------------------------|--------------------------------|--------------|--------------|------------------------|------------------------|
| DURING CONCRETE BUS PAD AND BASE REPAIR WORK | | | | | |
| 19 th Avenue and Taraval Street Intersection | | | | | |
| 19 th Ave. *(MC) | 7AM – 5PM (M-F) | 2@10' | 2@10' | - | - |
| | During concrete bus pad curing | 2@10' | 2@10' | - | - |
| | At Other Times | Full Roadway | Full Roadway | - | - |
| Taraval St. *(MC, MM) | 9AM – 3PM (M-F) | - | - | Closed @ (Except Muni) | Closed @ (Except Muni) |
| | At Other Times | - | - | Full Roadway | Full Roadway |
| CROSS STREETS for 19 th AVENUE | | | | | |
| Taraval St. (south crossing) *(MC, MM) ★ | 9AM – 3PM (M-F) | - | - | Closed @ (Except Muni) | Full Roadway |
| | At Other Times | - | - | Full Roadway | Full Roadway |
| Taraval St. (north crossing) *(MC, MM) ★ | 9AM – 3PM (M-F) | - | - | Full Roadway | Closed @ (Except Muni) |
| | At Other Times | - | - | Full Roadway | Full Roadway |

| Legend | |
|--------|-------------------------|
| | Type III Barricade |
| | 28" Traffic Cone |
| | Delineator |
| | Pedestrian Barricade |
| | Work Area |
| | Sign and Stand |
| | Direction of Travel |
| NTS | Not To Scale |
| TA/NS | Tow-Away/No Stopping |
| | Parking Control Officer |
| | Flagger |
| | Type I Barricade |
| | Flashing Beacon |

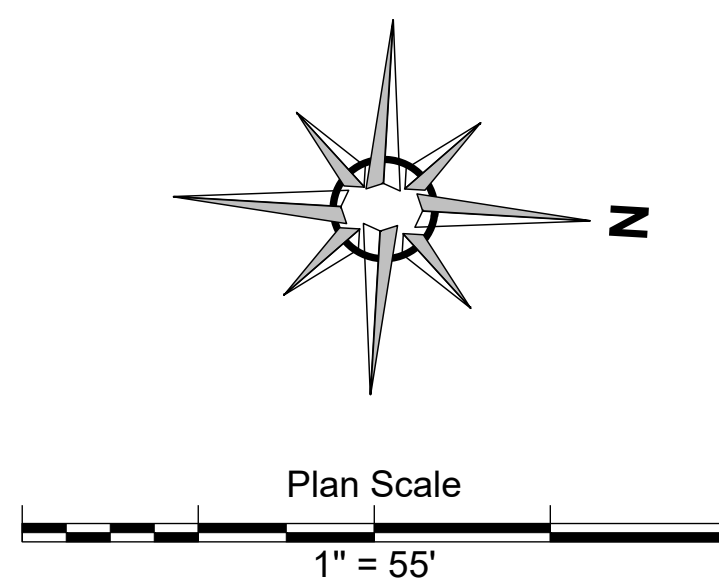

3450 3RD ST #3G
SAN FRANCISCO, CA 94124
415-206-1700 PHONE
415-206-1711 FAX
INFO@CMCTRAFFIC.COM

LICENSE NO 792059
CLASS A, 31, C21
WBE/SBE/LBE/DBE CERTIFIED
WWW.CMCTRAFFIC.COM

Date: 06/03/2021 Author: AM/DD Project: 19TH AVE (STATE ROUTE 1) COMBINED CITY PROJECT
Client: JMB CONSTRUCTION Location: SAN FRANCISCO TCP: 098
CMC Job #: 2530 REV: 1

- Comments:
- 1) WORK HOURS: SEE TRAFFIC LANE REQUIREMENTS TABLE
 - 2) CONTRACTOR TO VERIFY EXISTING STRIPING IS ACCURATE PRIOR TO START OF WORK.
 - 3) ALL TRAFFIC CONTROL SHALL CONFORM TO THE LATEST EDITION OF CA MUTCD.
 - 4) ALL TRAFFIC CONTROL DEVICES SHALL BE RETROREFLECTIVE IF SETUP DURING HOURS OF DARKNESS.
 - 5) MAINTAIN LOCAL ACCESS TO BUSINESSES AND RESIDENTS AT ALL TIME.
 - 6) THE CONTRACTOR SHALL NOT PREVENT OR DELAY THE OPERATION OF MASS TRANSIT VEHICLES AT ANY TIME.
 - 7) THE CONTRACTOR SHALL PERFORM THE APPROPRIATE MEASURES TO ENSURE THE SAFETY OF BICYCLISTS ON ALL STREET ON WHICH THERE IS CONSTRUCTION.
 - 8) THE CONTRACTOR SHALL NOTIFY MUNI AT LEAST 10 WORKING DAYS IN ADVANCE ABOUT CLOSING ANY BUS STOP AND FINALIZE LOCATION OF NEW TEMPORARY BUS STOP.
 - 9) THE CONTRACTOR WILL NEED TO POST SAN FRANCISCO POLICE OFFICERS (SFPD) AT THE INDICATED LOCATIONS.
